Contents

Key Messages i

1 Introduction 1

Overview of the Evaluation Scope and Activities 1
Report Structure 3

2 Lancaster University's ESIF -Funded Projects 4

Key Points 4
Introduction 4
Overview of the Projects 4
Funding Secured 6
Delivery Arrangements 7
Delivery Timescales 9
Building on Previous Experience

Key Messages

Introduction

This report has been prepared by ekosgen – an independent economic development consultancy – as part of the Summative Assessment of six ERDF projects which Lancaster University are leading and an overarching Impact Evaluation of all twelve ESIF projects Lancaster University deliver under the 2014-20 programme. At the time of commissioning, all projects were ongoing.

The evaluation secured insights into the performance of Lancaster University's ESIF funded projects to provide evidence of their efficiency, effectiveness and value for money, as well as identify lessons for future delivery. The assessment draws on:

- consultations with members of the project delivery teams;
- 189 telephone and online beneficiary survey responses;
- project management records to understand performance against targets to date and forecast;
- a working session with Lancaster University's Project Support Unit;
- calculation of economic impacts; and
- provision of practical learning points to inform future activities.

Key messages arising from the work are outlined below.

A Significant Funding Award and Strong Project Coverage

A £27.5m ESIF award was secured for the twelve projects within the assessment scope – £26.1m (95%) in ERDF and £1.4m (5%) ESF – as part of a total funding package in excess of £48m. Activity is delivered across three ERDF Priority Axes and one ESF Priority and in the Lancashire, Cumbria, Liverpool City Region and Cheshire and Warrington LEP areas,

This suggests, by December 2023, average cumulative impacts per beneficiary are forecast to be:

- 2.60 net jobs created or safeguarded;
- A £353,015 net uplift in turnover; and
- Increased net profit of £68,854.

These are strong returns and exceed those identified through the evaluation of 2007-2013 ERDF projects delivered by Lancaster University.

Value for money measures show that activities are efficiently delivering results and are securing a strong return on investment. Cost per job measures are in line with benchmarks (despite delivery during what has been a challenging context with reluctance for SMEs, particularly those at the smaller end of the scale, to commit to recruitment) and the return on investment of £18.52 per £1 to date rising to an estimated £28.55 per £1 of investment by the time activities conclude shows how support has enabled benefits to the economy to be many times the call on funding.

Lessons for Future Delivery

Lessons for the Grant Recipient
Lesson 1: It takes time to build momentum: Early output expenditure and output target s were optimistic, causing targets to be missed. Account is needed of the time it takes to recruit staff and approval timescales.
Lesson 2: Think about how beneficiaries will be targeted from the outset : Greater clarity regarding priority criteria and tailored engagement approaches/ sifts can ensure beneficiaries are best placed to benefit and achieve the target outcomes.
Lesson 3: Don't be afraid to make changes: Continuing to make adjustments in delivery approaches when necessary can help to return activity to target and improve the experience for both staff and benef1 (o)-1.6 13.3 (u.7 (e afo)13.3 (r)

1 Introduction

1.1 ekosgen – a specialist economic development consultancy with a strong background of work related to Structural Funds – was commissioned by Lancaster University to conduct Summative Assessments for the ERDF projects which Lancaster University are leading as well as an overarching Impact Evaluation of all the ESIF projects in which Lancaster University were actively involved. At the time of the work being commissioned, this included seven projects led by Lancaster University and five projects which Lancaster University plays an active role in but which are led by another organisation.

1.2 The Summative Assessments were commissioned in order to comply with funder requirements. Guidelines require the assessments – completed on an individual project basis – to: assess the effectiveness of each project; suggest improvements to the implementation and effectiveness of any future projects; document the development of the project and activities to help ensure lessons are learnt and support successful replication; document outcomes achieved through the project; and evaluate value for money the project achieved and / or will achieve by the point of completion.

1.3 The role of the overarching Impact Evaluation is wider. It provides an opportunity for Lancaster University to reflect on achievements across the programme of supported activities. The Impact Evaluation draws more widely on project experiences (from a delivery team, beneficiary and stakeholder perspective), reflections on the effectiveness of delivery models (and specifically what has worked well and less well), progress against financial and output targets, impacts, value for money and lessons and recommendations for future delivery. The quantified impacts help to demonstrate the return generated on investment, both to date and anticipated in future, highlighting the impacts of the University's activities on the regional economy.

Overview of the Evaluation S cope and AA

Ar v

a x Tw014.04 c 058lni.,-0 0 2.2 (a)-25(

Assessment Approach

1.5 The evaluation was undertaken between October 2018 and May 2019 and involved:

- Two phases of consultations with project delivery staff to understand how activities have been delivered in practice and lessons arising.
- Telephone consultations with a sample of stakeholders to understand external perceptions of the programme of supported activities and their added value.
- A significant programme of beneficiary consultation, cutting across all projects live at the time of the assessment, including telephone and online surveys and follow-up case study consultations. Each element captured beneficiaries' experiences of the support provided and benefits arising.
- Review of project management records to understand performance against targets to date and anticipated at the point projects conclude, any changes made and the reasons for them.
- A working session with Lancaster University's Project Support Unit to understand the package of support available to projects to ensure compliance with ESIF requirements.
- Calculation of economic impacts arising from project activities, both realised to date and anticipated in the future.
- The provision of practical learning points to inform future activities.

Issues Encountered

1.6 Two primary issues were encountered during the course of the assessment:

1. Due to the introduction of GDPR requirements part way through the delivery period, challenges were encountered in securing the engagement of beneficiaries in the research programme. By working through project leads, it was possible to eventually secure 189 survey responses from across the projects in scope. This figure exceeds the target set for 180 responses and equates to 27.7% of completed business assists recorded by the end of December 2018.
2. The impact assessment has been completed at a time when project activities are still underway – in six cases projects are due to run until 2020 or 2021. The true impacts of project activities are therefore yet to be realised and will increase over time, recognising that impacts often take some time to materialise. The assessment has therefore asked beneficiaries to comment on the impacts they have realised to date as a result of activities and those they anticipate experiencing in the future. Ongoing monitoring of project activities and impacts by Lancaster University will allow a fuller assessment to be established over time.

Impact E

- Priority Axis 4 (Supporting a shift towards the low carbon economy in all sectors) – four projects.
- Priority Axis 1 (Promoting research and innovation) – one project.
- Priority Axis 2.2 (Improved labour market relevance of education and training systems) – one project – the sole ESF award.

2.4 It is unusual for a university to only have a single award under Priority Axis 1 – given the research and innovation focus of this element of the programme – as part of a programme of activity of this scale. However, innovation is also supported through the Priority Axis 4 approvals and further funding opportunities under Priority Axis 1 are understood to currently be under investigation (see details under the Funding Secured sub-section).

2.5 The projects covered by the evaluation are:

Projects in Scope	
Priority Axis 1: Promoting Research and Innovation	
Project Title	Description
Cumbria Innovations Platform (ERDF)	Support to grow the Cumbrian economy by increasing innovation and productivity across the county's key economic sectors. The project delivers masterclasses, workshops, student placements, deep-technical assists and PhD supported R&D collaborations.
Priority Axis 3: Enhancing the Competitiveness of Small and Medium Sized Enterprises	
Project Title	Description
Health Innovation Campus (ERDF)	Focuses on the collaboration between SME's within the Lancashire region to enable cross-sector SME innovation of new products, processes and services into the growing health and care market place.

Eco-Innovation Cheshire and Warrington (ERDF)	36(1)]TJ -0.402 T043 -17387 TD [(C)6u (m)-3b (r)3.7 (i)12.6a(s)]TJ 0 Tc 0 Td (-)Tc -0.0(

Project Funding Packages		
Project Title	ERDF / ESF	Match

Project Delivery Models	
Delivery Model	ERDF Projects
Bespoke support: Businesses facing a specific growth or innovation need are provided with bespoke support. The support can take a variety of forms including dedicated research undertaken by PhD or Masters by research students, internships and student projects, or support from technical consultants. Projects are delivered on a 121 basis.	Eco-

2.22 Based on project timescales at the time of funding applications being made, all 12 projects were still in progress at the time of being commissioned to undertake the evaluation. Two projects (Lancashire Forum and U Start) were due to complete delivery in early 2019 (although extensions mean that they will now continue delivery beyond this date) and a further three were due to complete before the end of 2019 (Low Carbon Innovation Forum, Healthcare Business Connect Lancashire and Unite+). In contrast, half of the projects have activity end dates in 2020 and beyond meaning that a significant period of activity remains.

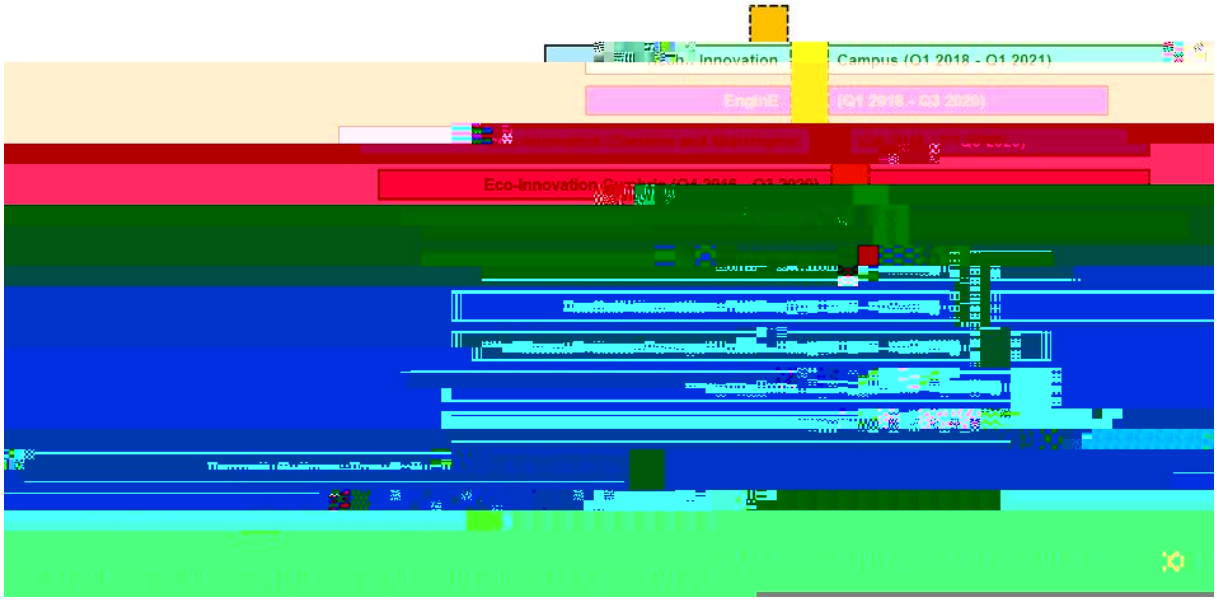

2.23 At the time of reporting, a series of project extensions have been agreed (for example for U Start and Lancashire Forum) and extensions have also been requested for others (for example Unite+ and EnginE). A new funding award (secured as a new stand-alone project to allow beneficiaries of the previous project to be supported again) has also been secured for the Cumbria Business Growth Hub project. The extended and new awards have typically been approved on a similar scale (in terms of finances and target outputs) as the initial funding awards and allow a further three years of activity to be delivered beyond the original project timescales. It is understood that an extension is not being sought for the Healthcare Business Connect Lancashire project. This is surprising given the development of the Health Innovation Campus and opportunity to generate a cluster of businesses and expertise.

2.24 Discussions with the Lancashire Forum and Cumbria Forum project teams suggest that, despite approvals allowing ongoing programmes of activity to be delivered, there will be a pause in the delivery of support sessions until the autumn. Although it is understood that this has been planned to allow a review of the level of academic engagement to be completed and new approaches to be confirmed, there is a risk that delivery momentum will be lost at a time when there are known levels of business demand. In contrast, the U Start contract extension has allowed for continuity of service.

Building on Previous Experience

2.25 Delivery of the ESIF projects within the scope of this assessment builds on Lancaster University's extensive track record of both securing and delivering ESIF funds and supporting knowledge exchange and business growth. The University has successfully delive

3 Strategic Context and Rationale for Intervention

Key Points

National Context

National Strategic Context and Project Alignment	
Strategic Drivers	Project s Response
Industrial Strategy (2017)[2] The UK Industrial Strategy 'Building a Britain Fit for the future' published in November 2017 identifies 'Five Foundations' for a prosperous and growing economy: 1. Ideas – R&D and innovation 2. People – skills, retraining and the labour market 3. Infrastru cture – transport, digital and housing 4. Business Environment – increasing SME productivity and start-ups 5. Places – tackling regional disparities in productivity and economic performance. The strategy also introduces 'Grand Challenges' which represent areas in which the UK has the opportunity to play a leading global role. They are: AI and Data Economy, Clean Growth, Aging Society and the Future of Mobility.	Lancaster University's ESIF project portfolio responds to multiple strands of the Industrial Strategy. For example, the Ideas strand is supported by projects including Healthcare Business Connect Lancashire and Cumbria Innovations Platform, the People strand by EnginE and the Business Environment strand by U Start and Unite+. Across all of the ESIF supported activities there is also potential to support the Places strand by reducing disparities in productivity and driving up economic performance with important achievements already evident in this area and further gains expected in the future. Considering the Grand Challenges, supported activities directly contribute to advances in Clean Growth (through Priority 4 activities) and an Ageing Society (through the Health Innovation Campus and Healthcare Business Connect Lancashire).
The Inclusive Growth Commission: Making our Economy Work for Everyone (2017)[3] In line with the plans laid out by the Prime Minister, the RSA Inclusive Growth Commission published a report setting out a framework for the UK to obtain an inclusive economy that supports productivity and economic growth. The intention is to: • Support more people into employment, reducing the strain on the welfare state and additional associated impacts of being unemployed; • Deliver changes to social and physical infrastructure (including education, housing, and connectivity); • Determine locally backed measures from local industrial strategies and businesses to develop a culture of inclusivity; and • Place inclusive growth at the heart of policies, through devolved powers.	Actions to support new business start-ups / enterprise alongside business growth and workforce development interventions allow the University to make a broad contribution to the inclusive growth agenda. Ways of working have broken down potential barriers between the University and the business community and have established networks that allow SMEs to understand the wider support network available to them (both formally and informally, e.g. through peer learning). Benefits are expected to include greater productivity, higher economic growth, the creation of new employment opportunities for local people and giving people an alternative to employment through enterprise.
Smart Specialisation in England (2015) The Smart Specialisation in England strategy provides a strategic framework for investments in research and innovation funded by ERDF. It recognises the value of	The Lancaster University project portfolio responds to the Smart Specialisation agenda by seeking to build on the University's areas of expertise and opportunities evident in the sub-regions it is working in. Supported activities have encouraged

[2] https://assets.publishing.service.gov.uk/government/uploads/system/uploads/attachment_data/file/664563/industrial-strategy-white-paper-web-ready-version.pdf

[3] https://www.thersa.org/globalassets/pdfs/reports/rsa_inclusive-growth-commission-final-report-march-2017.pdf

Impact Evaluation and Summative Assessment of ESIF-funded Pro .56 0 T3 [(f)2 (u)13.3 3.4 (nt)2 (o)tfsTd (-)Tj 0.004 7.267.002 Tw [(f)ET 60

Sub-National and Sub-Regional Context

Regional Strategic Context and Project Alignment	
Strategic Drivers	Project s Response
The Northern Powerhouse Partnership (2017) [5] The Northern Powerhouse Partnership was created to increase economic growth in the North of England and the UK economy as a whole by bringing key regions together to reduce the North-South imbalance. The report prioritised four key capabilities of the North to stimulate economic growth: • Education and Skills: Improvement of educational attainment by age 16 in order to develop the technical and higher levels demanded by employers • Infrastructure and Assets: Improved East-West connectivity to improve access of major cities. • International Competitiveness: Driving productivity growth through health innovation, advanced manufacturing and the digital economy. • Leadership and Learning: Using devolution to give local authorities the	

- Innovation excellence to enable Lancaster University and the University of Central Lancashire (UCLan) to support innovation in local economic sectors.
-

Impact E

The Knowledge Exchange Framework (KEF) (2017)[14] Announced as a new policy as part of the 2017 Industrial Strategy, and built upon the McMillan Review[15], the KEF aims (amongst other things) to increase the use of the expertise and skills of universities and their academics to provide solutions for commercial business needs over high growth sectors. The policy highlights that the UK has a number of high quality universities conducting world leading research, with public funding needing to go towards stimulating a collaborative culture between business and academia.	Collaborative working with businesses has been embedded across the Lancaster University project portfolio, allowing the sharing of skills and expertise and building relationships with the business base, including those in high growth sectors. Cross faculty delivery for a number of projects has ensured that the business base has been able to access the expertise they need from a diverse range of perspectives. Projects have also been designed to build on recognised research strengths, for example the expertise of the Centre for Global Eco-Innovation for delivery of Priority 4 projects.

The Dowling Review of Business -University Research Collaboration (2015) [16]

The Dowling Review (2015) considered how the government can better support the relationship between businesses in the UK and researchers at world-leading UK universities. 4he revi(ed bhsp (G)8.6 us (e)13.3 uiperf)1.9 ((ed)]13.annt)2 (he gaper)3.7 (t)2 T(r)3.6 n ()13.4 (i)-1.7 (n t)2)(h)13.3 (e2U)6 iasest to[(x)24 de he 6entr flip f1.6 (a)13.4 (((f)1.9 d-2.7

Continued Strategic Relevance

3.4 Due to the locally embedded nature of Lancaster University's activities and strong strategic rationales for intervention at the outset of projects, clustered around recognised priorities for the Lancashire economy and wider North West, supported projects have remained strategically relevant. The University has been able to apply its expertise to emerging opportunities and long standing ambitions in innovation, the low carbon agenda and supporting business growth and through its activities has demonstrated the wider role the institution plays within the economy.

3.5 As examples, the activities of the Centre for Global Eco-Innovation are already supportive of the opportunities identified through the Coastal Arc Partnership for Clean and Sustainable Growth and the North West Nuclear Arc Science and Innovation Audit as well as national l (t)-13.a-25.2 (y)7 (as)-dn12.2 (l)3.1

Setting Objectives

3.11 The logic models set out objectives for each project. In the main, these objectives are specific and measurable, with quantified targets set out in the outputs, outcomes and impacts section. They link back clearly to the issues highlighted in the context and market failures section, e.g. the 'institutional deficiencies' in SMEs identified in the Lancashire Forum logic model will be tackled through reducing non-technical skills gaps (e.g. leadership development). There are a small number of projects where the objectives are less specific (e.g. Cumbria Growth Hub - "enhancing the growth and competitiveness of Cumbrian SMEs and supporting job creation through review and action planning leading to personalised packages of support drawing on direct delivery through this project and support available more widely.")

3.12))

4 Project Performance

Key Points

- Slippage in project activity – primarily due to delays in contracting (beyond the University's control) and staff recruitment – means that expenditure has been behind target. By the end of December 2018, total spend of £14.9m had been reported against at target of £16.6m. However, discussions with project leads suggest that, in a number of cases, the position had improved by the end of March 2019 claims.
- Where variances have been required they have been actioned and the Project Support Unit – working with project teams – remain alert to the need to continue to review performance.
- Forecasts suggest eight of the 12 projects are expected to satisfy financial targets across their duration, while three projects are forecast to underspend due to the impact of irrecoverable slippage in programmes of activity.
-

4.4 Ten out of the 12 projects had underspent against targets for spend to the end of December 2018, leading to an overall underspend against target of around £1.68 million. Lower than anticipated expenditure levels have been due, primarily, to later than anticipated project approvals being secured (impacting on ten of the projects) with a consequent impact on the timing of recruitment (with a funding commitment required ahead of Lancaster University and partner organisations being able to make appointments) and therefore the ability to draw down funding. Steps are being taken by project staff wherever possible to return expenditure to target but where this is not possible, variance requests are being made to allow the programme of activity to be managed and the funder to be made aware of potential longer term implications for expenditure (see details later in this section).

4.5 The programme wide and project by project progress against expenditure targets is summarised below with brief explanations of the primary causes for variations against targets.

Financial targets to end of Q4 2018 against actual expenditure totals				
	Target to Q4 2018	Actual to Q4 2018	Difference	Reason for Difference
Health Innovation Campus	£3,245,799	£3,559,615	+£313,816	

Spend by Priority Axis

4.6 Overall the projects falling under ERDF Priority Axes 1 and 3 and ESF Priority Axis 2.2 had underspent at the time of the December 2018 claims being submitted, while overall projects under Priority Axis 4 are on target with 99% of the target spent by the end of 2018. EnginE, the only ESF

Expenditure Forecasts

4.8 During 2019, 2020 and 2021, to project completion, £0.5m more is expected to be spent than was initially contracted across these years (keeping within overall project budgets) reflecting the underspend to date and plans to utilise allocations. In 2019 there is expected to be a significant

Financial Profile to Date and Forecast

Overall Output Profile [20]														
Project Title	C01	C04	C05	C08	C25	C26	C28	C29	C34	P02	P11	P13	R9	C023
CUSP	120	120		25		60	10	50						
Health Innovation Campus	300	300		35	50	300	25	50		3,750				
U Start	86	86	86	87			5				250			
Healthcare Business Connect Lancashire	94	94	23	61			12	25				9		
Unite+*	100	100	16	40				15						
Lancashire Forum	210	210		88				27						

- The number of new enterprises supported (C05) had reached 59 opposed to the target of 107 contracted to the end of 2018 (59%). One project manager stated that in part, this is due to the definition of 'new enterprises' used by MHCLG, which uses a time-based definition, rather than looking at the business' state of development[22].

- The number of enterprises cooperating with research entities (C26) is behind profile with 133 against a target of 208 (64%). The main reason for underperformance highlighted by many of the projects, as noted above, was a lack of clarity about how this output could be evidenced. Work is now underway to agree a cross-University definition which all projects will use, and gather the necessary evidence from companies to submit a backlog of output claims.

Targets to the end of Q4 2018 against achieved, by Priority Axis								
	Priority Axis 1		Priority Axis 3		Priority Axis 4		ESF Priority Axis 2.2	
Outputs	Achieved	% of target achieved	Achieved	% of target achieved	Achieved	% of target achieved	Achieved	% of target achieved
C01	91	121%	453	78%	138	113%		
C04	91	121%	453	78%				
C05			51	50%	8	89%		
C08	3	43%	109	43%				
C26	27	77%	0					

Impact E

5 Effectiveness of Project Delivery and Management Arrangements

Key Points

- Partnership working has allowed Lancaster University to successfully expand its profile of ESIF projects, by geography and subject areas. The relationships established have been clearly articulated through Service Level Agreements with day to day activities typically delivered in parallel with partners.
- Beneficiary engagement routes have proved effective and there is evidence of both referrals being made into and on from ESIF supported schemes, supporting beneficiaries to access the support they need to succeed.
- Whilst each delivery approach can present advantages and disadvantages, the combined approaches are fit for purpose with tailored models ensuring each project has been able to take an approach that best meet their needs. A willingness to adapt approaches where necessary is positive and a focus on peer learning has been highlighted as a particular strength by beneficiaries.
- The receipt of ESIF resources has allowed Lancaster University to add value to its in-house support offer and services across the sub-regions it is operating in. Delivery of the same breadth and scale of activity would not be possible in the absence of ESIF funding and beneficiary feedback suggests projects are filling a gap in provision.
- Lancaster University has robust processes in place to manage ESIF funding with the role of the Project Support Unit central to ensure compliance and consistency of approaches across the project portfolio. The Unit's activities are valuable to protect the reputation of the University and minimise the scope for clawback or refused claims.

Introduction

5.1 This section considers how the ESIF projects have been delivered in practice. It sets out an assessment of how partners have worked together, the advantages and disadvantages of the delivery approaches that have been applied and steps taken to manage ESIF resources across the prograci-4.3 (r)-Iep2 (t)-he

5.8 This combination of approaches has helped to ensure that Lancaster University has been able to secure both the number and characteristics of beneficiaries required for varied project types with the volume of beneficiaries building across the portfolio. In general, project managers were happy with the number and quality of businesses engaged with their projects.

> "Boost referrals have been like gold dust…we have got some cracking companies."
>
> "There has been no let-up in the number of enquiries."

5.9 Consultations suggest that marketing materials and approaches have been tailored to reflect previous experience with project team comments including:

> "Headlines like apprenticeships and training sometimes fall on deaf ears…we talk about the benefits of workforce development first."
>
> "We have developed a number of different straplines to engage the right types of organisations."

Beneficiary Experience

5.10 Survey results show that beneficiary experience of the initial engagement process has been positive with:

- 93% satisfied or very satisfied with the quality of the information about the available support; and
- 92% satisfied or very satisfied with the:
  - clarity of the eligibility criteria for receiving support;
  - ease of the application process; and
  - length of time taken between initial inquiry to working with the project.

Onward Referrals

5.11 Projects have also been alert to the need to refer beneficiaries on to further support services on the completion of support packages. This includes:

- Referrals on to other ERDF funded projects being delivered by the University (for example a number of Cumbria Forum beneficiaries have gone on to benefit from CUSP and Health Innovation Campus beneficiaries have accessed Healthcare Business Connect Lancashire services);

- Considering opportunities to maintain working relationships outside ERDF support (for example through the 'in between workshops' where businesses from the different Low Carbon Innovation Forum cohorts are introduced to each other, or by inviting past participants to take part in Lancaster University Management School's regular masterclasses or other networking events); and

- Referrals to external business support providers (such as access to finance support available through Lancashire Boost from U Start and Lancashire Forum referrals for mentoring support).

5.12 This suggests that the project teams are alert to ensuring businesses secure the support they need and are keen to identify support packages to best suit their needs. However, referrals within the ULancashi16.1 ( )-10.6 p (p)-12.2e (ar)-6.3 ento bdspm wt.

activity – ideally through a central contact point that can support a seamless journey for beneficiaries and effective signposting – there appears to remain an opportunity for both businesses and Lancaster

- More intensive forms of support are proposed to be offered under the Health Innovation Campus revenue project from next year through a delivery approach that is more aligned to the cohort working model, focusing on specific topics of interest to beneficiaries.

5.16 It is clear that staff are not afraid to make changes where they are needed to ensure projects can deliver to their potential. Examples of comments made include:

> "We have tried to be flexible to support the needs of the business."
>
> "We have had to make some changes."
>
> "We are constantly evolving."
>
> "We have got the momentum going. We now have better engagement with schools and faculties and have a regular workshop programme."

5.17 It will be important that this learning informs the future design and implementation of projects with signs that the project teams are already planning accordingly. As the University starts to look beyond ESIF funding, there may also be scope to secure greater flexibility in delivery methods, particularly as performance measures change. Whilst the University is already keen to focus on the achievement of impacts rather than purely the achievement of contracted output targets, the scope to tailor delivery approaches accordingly may alter as new funding streams are introduced.

Beneficiary Experiences

5.18 Programme wide reflections on delivery models are broadly supported by beneficiaries with 99% of those surveyed agreeing that the delivery approaches are/ were fit for purpose. The highest levels of satisfaction were reported with the workshops and business diagnostic and peer learning (please refer to Section 6 for further details).

5.19 When asked an open question about the strengths of their project experience, prominent themes identified by beneficiaries were the benefits of peer support and networking with like-minded businesses. The diverse range of attendees that were involving in a number of the projects allowed for beneficiaries to gain valuable insights into their business looking from another perspective. Furthermore, many businesses also stated that despite a diverse group of businesses, many shared the same challenges when running and growing a small business, allowing for connections to be made that may not have existed if it was not for the support programmes.

5.20 Examples of feedback provided are outlined below and further commentary on this theme is provided below.

"I wouldn't be in business without the team at Lancaster…. The enthusiasm of the team has helped keep me motivated when I was lacking confidence to move forward. I can't fault them."

"An excellent service could not have done it without them"

"The project has helped me reassess my organisation, the project came along just at the right time

Strategic Alignment and Added Value

Adding to the In- House Offer

5.26 The award of ESIF resources has allowed the University to deliver a programme of activities that would not be possible in the absence of external funding. Whilst the University takes its civic society role seriously and recognises the value that it can add to local communities and economies, there is a limit to what can be delivered in the absence of external support. A series of internal support services (e.g. enterprise support and joint working with industry) are evident but they do not operate on the same scale or breadth as has been possible through ESIF funding.

5.27 As a consequence, ESIF resources have added significant value to what could be delivered by the institution unsupported, predominantly in the form of the scale of activity. The number of staff posts assigned to the delivery of ESIF activity means that it would not be possible to continue the same scale of activity in the absence of external funding.

Aligned and Added Value Services

5.28 The partnership approach taken to the delivery of many of the ESIF funded projects and Lancaster University's wider network of contacts means that there is coordination in the programme of activities being delivered. The University has also drawn on a network of external contacts (for example to deliver specialist workshops) that offer beneficiaries a different perspective to what would be possible if the University was to deliver activities alone. Consultations suggest that ESIF projects are seen to add value to the service offer and respond to strategic priorities in Lancashire and beyond (where applicable).

5.29 Stakeholders welcomed the role that the University plays in the local economy - both through its delivery of business support projects, and through its wider lobbying and influencing role. No concerns were identified regarding the potential duplication of activity with Lancaster University products seen to be distinct from the other available through sources such as the Growth Hubs.

> "Having a champion and ambassador for the area is really valuable, especially when it's a really credible, export body which is providing services to business. The University's engagement on the wider issues is phenomenal."

Beneficiary Perspectives

5.30 Beneficiaries were asked what they would have done in the absence of the ESIF project they had accessed. Under half (45%) of respondents reported they would have sought support from (w)12.3 (de-13.1 (k08 0 T1F 16.1 ( )-1o-37.723 -1 Tw 12.19-13.2 (r)-6.3 (o)11.8 (3.1 (c)-8l)3e-13.1 (p (c)-8l)(hen)-1on1

5.31 The breadth and scale of benefits reported by beneficiaries and apparently high levels of additionality (see Section 7) suggests

Evaluator Assessment

5.40 It is the evaluator's view that the PSU is an important element of Lancaster University's project management arrangements. Its activities seek to make the ESIF reporting process as smooth as possible and reduce the audit pressures placed on project teams. The arrangements help to ensure that all projects comply with funder requirements, allowing any potential issues to be identified and addressed early and reducing the risk of challenges being raised through either the claims or audit process.

5.41 The absence of clawback and limited claims queries (none of which have been challenging to overcome) suggest that the system is effective and lessons are effectively being shared across the project teams. A small charge included within ESIF project costs generated a funding allocation of £xxxxx to fund the team – xx% of the ESIF allocation. The return on this investment – through time saved on challenged claims and the risk of clawback – would be anticipated to outweigh the upfront cost.

Project Monitoring and Reporting

5.42 Consistent monitoring approaches

Survey Sample

6.3 Across the telephone and online survey a total of 189 responses[23] were secured; 109 telephone survey respondents and 80 online respondents. To put the figure into context, the sample equates to almost 28% of beneficiaries who had completed a business assist by the end of December 2018. Complying with General Data Protection Regulations (GDPR) meant the telephone survey sample was shaped by the willingness of beneficiaries to give permission to project leads for their contact details to be shared with the evaluators

ea.1 EMC())-6.3 ((w)9.2 (as)-8.1 (o(p)-12.3 eon t)-1.1 (o(a)-12.3 (l)-8.9 (l)3.1 p)]TJ 0.0

Reasons for Engagement

6.5 The chart below summarised the main reasons beneficiaries identified for seeking support. The most common support requirement was to assist with was business strategy/ business growth (52%) – reflecting that businesses made up the majority (91%) of respondents. Support with new products or product development was the second most common reason (recorded by 91 respondents (49%)), followed by leadership/management/commercial skills development and building a network of contacts (both accounting for 46% of responses). Reasons cited under the 'Other' category (in each case reported by one beneficiary) included R&D, ideas for other business opportunities and reducing carbon footprint, branding, building an evidence base and marketing advice.

6.6 Reflecting the varied foci of projects, the reasons for seeking support varied across the respondents. For example, beneficiaries of the Lancashire Forum project most commonly sought support to develop leadership/management/commercial skills, while beneficiaries of the Health Innovation Campus most commonly stated that they were seeking to develop new products or processes.

Experience of Initial Project Engagement

6.7 Respondents became aware of the support available through a variety of means with the most common being directly approached by someone at Lancaster University, accounting for almost a third of those surveyed. The nex

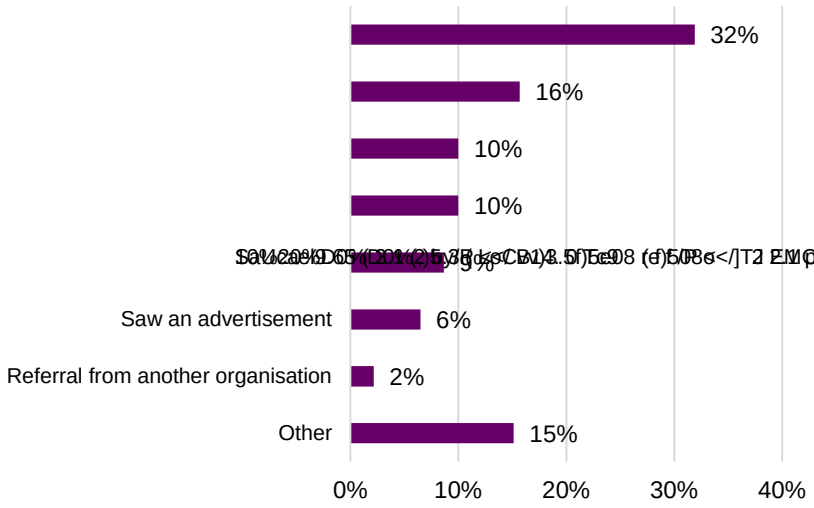

6.8 The respondents were asked to rate aspects of the initial/early contact they had with the project on a scale from 1 to 5 with 1 being very dissatisfied and 5 being very satisfied. The level of satisfaction was overwhelmingly positive. Between 93% and 92% of respondents satisfied or very satisfied with the: quality of the information about the available support; clarity of the eligibility criteria for receiving support; ease of the application process; and length of time taken between initial inquiry to working with the project.

6.9 None of those surveyed reported being very dissatisfied with any of the statements shown in the above chart, while between 1% and 2% of respondents reported being dissatisfied with the statements regarding initial/ early project contact. These beneficiaries were across four of the projects[24]. This is a positive finding as beneficiaries' initial experience of engaging with project support can have a lasting impact on their overall perception of the support received.

[24] Unite+, LoCaL-i, U Start and Eco Innovation Cumbria

Satisfaction with Support Received

Overall Satisfaction

6.10 In terms of the support received, 96% of respondents were happy with the support provided by their project. Projects which reported the highest satisfaction rate (100%) in the order of largest number of respondents were: Cumbria Innovations Platform, Cumbria Forum, Unite+, Health Care Business Connect Lancashire, Low Carbon Eco-Innovatory, Eco-Innovation Cheshire and Warrington.

Overall dissatisfaction levels were low. The highest number of respondents who were dissatisfied about the support they received overall was two out of the 14 respondents for the Health Innovation Campus. One, who had attended a workshop, stated there was “not enough time to provide solutions”.

In limited instances there may be a requirement to manage expectationsay b6[(not)-9 (i -0)2.9 (i 7Tj 2 583 hm.4 6.5

[redacted]

survey work, and
18% of those who
17 used the word

eam at Lancaster:



"Initial support was good, but the project advisor's interest waned quickly. They didn't put in the right amount of time and effort into the research, and they lost focus on the objectives."

"However, post project support was unsatisfactory, there was no follow up."

"After that, I sadly didn't receive any further response, which was a real shame. I also felt unsure whether I could attend workshops or whether they were meant for people further on in the project. It wasn't so well organised on that front - maybe advice about which meetings were available would have helped."

"However, the support should be longer in order to maximise and implement the support."

"…I did not think the course was long enough."

"…the duration of the support could be a bit longer."

6.24 These points are reflected in the potential improvements outlined in Section 8.

7 Project Impacts and Value for Money

Key Points

- Participation in Lancaster University's ESIF funded projects has generated wide ranging benefits for beneficiaries including improved commercial performance and prospects and softer benefits such as increased market awareness and improved business connections.

- Benefits for the University include a raised profile in the sub-regions it is working in and the

- Establishing greater understanding of the purchasing approaches of target sectors and businesses to allow opportunities to be targeted.

- Securing external funding support (for example from Innovate UK in the case of a Healthcare Business Connect Lancashire beneficiary) to progress their product ideas.

- Establishing new contacts within client organisations and potential supply chains and, ultimately securing new orders / business opportunities.

- New products or services being taken to market, for example 13 businesses supported by the Centre for Global Eco-Innovation projects[26] identified the development of a new product, process or service as a benefit of their involvement and nine businesses had already experienced an improvement in their existing products and services.

7.3 Although not all projects had defined targets to generate commercial benefits, it is clear that

strength of the University and individual project teams. Improved business networks/ collaboration, raised company profile, sustained employment levels and a stronger and more stable business were also reported to have been achieved by at least half of those surveyed.

7.12 Survey results for the Cumbria Innovations Platform, Lancashire Forum, Unite+ and Eco-Innovation Cheshire and Warrington projects revealed that 100% of respondents achieved or anticipated an increased likelihood of engaging with the University on other projects. These findings suggest that, for many, involvement in an ESIF project may be towards the start of their support journey with an appetite to go on to access other services.

7.13 When beneficiaries were asked, in their own words, what the biggest impact of participating in ESIF funded projects has been on their business th(neI0A)y3.2 (n)-6-6-6-6-een(ne9)-12 ew 1.606m0 1(2)12 ((gene

7.14 Sample responses provided by respondents, linked to these prominent themes, include:

> "My self-confidence has increased, I've got the fire back in my belly."
>
> "A trusted network of peers, who we can turn to for advice or support."
>
> "[the biggest impact has been] the Networking opportunities."
>
> "[the biggest impact has been] continued peer groups and networks established."
>
> "The peer support network has been fantastic."

7.20 In addition, 21 comments highlighted the benefit of working with the University, with many stating they would be happy to work with the University again. Examples of feedback provided include:

> "[the biggest impact has been] the opportunity to engage with the staff at the University."
>
> "Overall, very valuable and have made plans to work with the University again."
>
> "We would be more than happy to work with the University again."
>
> "The enthusiasm of the team has helped keep me motivated when I was lacking confidence to move forward. I can't fault them."
>
> " The research would have not been done or been very costly if it wasn't for the student project."

Wider Impacts

7.26 Stakeholders are broadly positive about the role that Lancaster University – through the delivery of ESIF supported projects – play in the local economy. Although many of those consulted were only familiar with distinct elements of the offer, the package of support has helped Lancaster University to raise its profile amongst stakeholders and businesses with partnership working in support of project delivery, allowing wider coverage to be secured than may otherwise have been the case.

7.27 The offer the University has been able to make to students has also been enhanced with one consultee commenting: "As a student, the benefits you get from engaging with our programmes is far wider than their academic programme of study." Provision of purely an academic offer is no longer sufficient in a competitive marketplace with the wider support offer, in part supported by ESIF resources, helping Lancaster University to retain a competitive advantage and demonstrate the potential students the wider advantages that they can secure by studying there. In addition, the University's network of SME contacts has continued to expand, offering potential for further collaborative working of mutual benefit.

7.28 Consultations completed during the course of the evaluation emphasise that Lancaster University are not delivering services purely to draw down resources and satisfy ESIF targets – they want to provide a valuable service to support individuals and businesses to succeed.374 0 Td (–)Tje(her)5.( )0.6 (h

7.34 Although these measures are not captured as direct outputs of ERDF, using the programme's indicators, they provide a good indication of the wider impacts that participating in ERDF projects are generating for beneficiaries.

7.35 The findings suggest that each beneficiary receiving support through Lancaster University's ERDF projects generates the following gross impacts on average:

Additionality Adjustments		
Factor	Adjustment	Rationale
Deadweight	40.0%	Adjusted down from the mean regional benchmark for business development & competitiveness (45%) in response to survey feedback
Displacement		

7.43 In addition, the survey found that:

- Sixty two respondents (33.7%) expect to experience uplifts in turnover totalling £132m (£105m once optimism bias has been applied); and
- 62 expect to record an increase in profit, this totalled £21.4m (the sum of only fifty increases as 12 were reported as percentages) (£17.1m once optimism bias has been applied).

7.44 Aggregating these figures up to the total forecast beneficiary base of 1,245 anticipated at the point of project closure, suggests that total benefits (following consideration of optimism bias) will be in the region of:

- A £712m uplift in sales / turnover; and
- A £144m uplift in profit.

7.45 The findings suggest that each beneficiary receiving support through Lancaster University's ERDF projects is expected to generate the following gross impacts on average going forward:

- 7.43 jobs created or safeguarded;
- A £572,175 uplift in turnover; and
- Increased profit of £115,549.

7.46 Forecast benefits are summarised below.

Gross Anticipated Benefits *	Anticipated by surveyed businesses

- Increased profit of £68,106.

Total Benefits

7.49 Taking account of the benefits reported to date and anticipated in future, following an adjustment for optimism bias, suggests the following scale of benefits resulting from programme activities:

- Over 3,200 net FTEs created/safeguarded;
- A net turnover impact of £440m; and
- A net profit increase of £86m.

7.50 Based on the figures above, average cumulative impacts per beneficiary are forecast to be:

- 2.60 net jobs created or safeguarded;
- A £353,015 net uplift in turnover; and
- Increased net profit of £68,854.

7.51 These are strong returns and exceed those identified through the evaluation of 2007-2013 ERDF projects delivered by Lancaster University.

GVA Impact

7.52 The GVA impacts have been estimated based on the employment benefits of the programme, taking account of both created and sustained employment. A GVA per FTE figure of £63,204 has been applied – the mean GVA per FTE for the North West based on ONS GVA data and Business Register and Employment Survey employment data for 2017, taking account of all sectors of the economy to determine an average contribution. Multiplying the number of supported posts by the GVA per FTE figure generates the forecast GVA impact per annum.

7.53 The GVA benefits of the supported roles are assumed to persist for three years. This is a typical benchmark for interventions taken from the 2014 HCA Additionality Guidance. The resulting gross GVA benefit of the 1,547 gross jobs created/safeguarded to date is estimated to be £292.6m. Combined with forecast employment GVA impacts an estimate of £1.04bn of impacts is reached.

7.54 The same level of gross to net adjustments have been made to the GVA benefits as the employment benefits (see earlier details). A discount rate of 3.5% has also been applied across the assessment period to determine the net present value of the GVA benefits, as summarised below.

GVA Impacts			
	Current	Future	Combined
Gross	£293m	£747m	£1.04bn
Net			

Value for Money

7.55 The value for money assessment has taken account of two core measures: the cost per job generated by project activities; and the return on public investment. The ESIF drawn down by the end of 2018 was £8.69m, and the total ERDF funding forecast to be spent by the projects is £20.0m. These totals are divided by the number of jobs to determine the cost per job figure for both to date and the future jobs.

Cost per job		
ERDF Cost per Job	Current	Current and Future

8 Identified Challenges and Potential Improvements

Key Points

- Overall, ESIF supported projects are being delivered effectively with limited challenges encountered given the scale of activity.
- Projects teams are alert to and open about the challenges they have encountered and none have proved insurmountable.
- Managing beneficiary expectations may be necessary as the programme of activities continues, reflecting constraints on the funding available and the fact that, in many instances, Lancaster University already goes beyond the 12 hour assist required for ERDF outputs capture.
- A limited number of potential improvements have been identified to inform forward planning, including scope to increase academic engagement, greater targeting of beneficiaries and recognising distance travelled by beneficiaries.
- Many of the issues arising may not be resolvable within the confines of ESIF funding but may present factors that are worthy of consideration in the planning of future funding streams such as the Shared Prosperity Fund.

Introduction

8.1 In conducting the evaluation, consideration has been given to emerging themes around delivery experiences and the potential to improve approaches going forward.

Potential Improvements

Delivery Team Perspectives

8.5 As noted elsewhere in this report, the Lancaster University team remain alert to the effectiveness of delivery approaches and the opportunity to make improvements where necessary. Delivery continues to evolve to reflect this and as projects come to an end and both extensions and new project proposals are developed, opportunities can be taken to make changes.

8.6 Potential improvements identified through the evaluation include:

3. Advisor interest in business needs: Some beneficiaries reported that although the university advisors' initial support was good they felt that they later lost focus with their business and their goals. Issues with the level of interaction with the business, with meetings dying down after the initial stages and one beneficiary having to "nudge for updates on progress" were also reported. Additionally, there were expectations that "the students' tutor to be more engaged with them [student] rather than just leaving them to do it".

8.10 Other notable themes included comments relating to: bureaucracy due to the number of forms to be completed; limited awareness of the full range of workshops available; a desire for post-support follow up; and the quality of students received as part of research projects.

8.11 Whilst many of the suggested improvements could not be accommodated within the confines of ESIF support, new funding regimes (such as the forthcoming Shared Prosperity Fund) do provide an opportunity to design arrangements in response to experience and the feedback of both

9 Conclusions and Lessons Learned

Conclusions

Building on a Strong Track Record

9.1 The 2014-20 programme has provided an important opportunity for Lancaster University to continue to build on its expertise and reputation in the delivery of ESIF activities. By working with partner organisations, including other higher education institutions, the University has been able to both share its expertise and learn from the experience of others while gaining exposure across four of the North West's sub-regions – an important distinction for the latest programme period.

9.2 Activity suggests that Lancaster University remains at the forefront of ESIF delivery in the region. The addition of an ESF project to the 2014-20 portfolio has been an important addition, allowing the University to explore opportunities to support advances in higher-level skills – a core objective of the institution – as part of its externally funded activities. As the EnginE project manager commented: "ESF is a new area for the university but it is an important one", with strong growth evident nationally in Level 7 apprenticeship demand noted in particular. Further ESIF funding opportunities currently being explored (although focused on ERDF rather than ESF) will allow further gains to be made, alongside the ongoing delivery of projects within this impact assessment scope.

Making Important Progress against Targets

9.3 The impact evaluation was commissioned at a time when all projects were continuing delivery. Although progress was behind target for a number of indicators at the time of the December 2018 claims being submitted, the majority of project managers are confident that they will satisfy their indicator targets by the time of closure and noted that a number of projects had improved performance relative to targets by the time of the March 2019 claims. Consultations suggest that – on the whole – projects have a strong pipeline of beneficiaries in place to allow targets to be satisfied and / or demand for services continues to be demonstrated through marketing and engagement activities.

9.4 Delays in project approvals were beyond the University's control and undoubtedly impacted on the start date of a number of projects. Later than anticipated recruitment and some staff turnover (inevitable on a programme of activity this size and particularly when project extensions are agreed close to the point of original contracts coming to an end) mean that – on projects dominated by staffing costs – many projects are behind their expenditure targets and will now deliver programmes of activity at a lower cost than envisaged at the point funding applications were made. With achievements to the end of December 2018 including 682 enterprises assisted, 133 businesses supported to develop new to the firm products and 243 potential entrepreneurs assisted to be enterprise ready, ESIF investment

Successful Delivery Approaches (with changes being made where necessary)

Lesson 3: ESIF activities should not be viewed in isolation: Lancaster University is already alert to the wider opportunities to engage with businesses and individuals beyond individual ESIF project engagement. However, this could go further with a defined referral system. There is a recognised appetite from beneficiaries to continue their engagement with the University but achieving this requires a smooth transition, if the full value (for both beneficiaries and the University) is to be secured. A central point of contact with the ability to make connections between project teams and academics would support this process, helping to identify opportunities for advantages to be captured for all parties.

Lesson 4: Strategic positioning should be considered : Whilst the broad portfolio of supported projects can be seen as a positive, when positioning for new funding streams it will be important for Lancaster University to be able to demonstrate its particular strengths. A sectoral focus is likely to form part of successful project positioning with growing specialisms in low carbon and health innovation (as examples) strategically aligned and distinct, although in the latter case, the decision not to seek an extension to the Healthcare Business Connect Lancashire project is a surprise.

Lessons for Policy Makers

9.19 The following primary lessons have been identified for policy makers from across all the ESIF projects within this assessment scope:

Lesson 1: Delays in project approvals impact on deliverability: Many of the projects Lancaster University is delivering secured approvals later than anticipated at the time submissions were made. This impacts on the ability of projects to hit their targets and deliver within agreed timescales. Where significant delays are encountered, opportunities for variances to be automatically applied should be explored, for example to allow the same period of staff time to be captured in project costs – a factor that cannot be 'caught up' once a late start occurs.

Lesson 2: Short term funding awards impact on the continuity of services: The challenges faced by projects differ dependent on the nature of activities being taken forward. For those projects (such as LoCaL-i, Low Carbon Eco-Innovatory project, Eco Innovation Cumbria and Eco-Innovation Cheshire and Warrington) that provide support to businesses by providing a dedicated PhD researcher to investigate a specific topic, a three year funding award means that placements need to be fixed at an early stage in the project, through a single intake, to allow achievements to be secured. For other projects (such as Cumbria Forum), the lack of certainty around future resourcing as three year contracts come to an end can result in staff turnover and the loss of momentum in delivery that it can be challenging to recover.

Lesson 3: The offer of a lead in period would allow strong performance from the start: Linked to lesson 1 for the grant recipient and others delivering similar projects, approval processes assume that projects can quickly build momentum from the point of approval. Where approvals need to be in place ahead of staff being recruited there is an inevitable lag in activity starting that causes projects to be behind profile from an early stage. Building a lead in period into contract awards that allow preparations to be made

Annex 1: Lancaster University Led Project Headline Findings

Annex 1a – LoCaL-i

Description of the Project

This project aims to increase innovation and adoption of low carbon technologies by enabling businesses across all sectors to develop new products and markets through research and innovation and the development of capacity for eco-innovation – leading to growth of the low carbon economy in Lancashire.

Procte

(o)1758.28 224>BDC7 (s2[64.9* e)11 g5 (p1-2 (a)11.3r)3.7 (oj)12.7 3.4 (nt)2 (o)176.344Tc -0.Tt.26fsAsq 241 0.0032.12t59.28 2 (

Comments

- "the project has made us realise that however small the enterprise, through a number of small changes, we can reduce our carbon footprint at very little cost."
- "Very happy with the project. Regular contact by telephone/skype/face to face. Was good to use the expertise of staff and students in designing green powered vehicles and being able to use their facilities. We felt that the projects could be larger, and it would be great to come away with an actual product rather than just the plans on paper. There is scope for the university to help on the practical side of things, not just the theory."
- "Quite pleased with the progress. Might need to steer it back a bit more towards their goals - what they need from it is changing a bit. It is coming up with some interesting stuff and I appreciate that these projects have to be unique and innovative. Have to nudge for updates of the progress."

Case Study

Case Study: Euriscus

With offices in Preston and London, Euriscus are an additive manufacturing (3D printing) and software company made up of three employees with more than 15 years' experience in the sector. They also offer marketing services to businesses in the dermatology and skincare sector.

The company has worked with Lancaster University on a number of different projects over the years. Euriscus heard about the LoCaL-i project through a contact within the University's Department of Engineering in 2017. After a very positive initial meeting with the programme team, a PhD research project was developed to explore the potential use of plant based materials for additive manufacturing, an innovation that would be more sustainable than current approaches which are dependent on the use of plastics-based materials. If successful, the new approach could provide significant business opportunities for Euriscus within the additive manufacturing sector, which is part of a growing industry of transition to 3D printing as a mean of mass production.

By working in collaboration with Lancaster University, Euriscus has benefitted from the wide array of academic expertise and facilities on campus which would have been costly and challenging to acquire without the support of the project. They commented: "[It] gives a tiny company access to resources that even a much bigger company cannot access".

The project is still in the research stage with its outcomes shaping the trajectory of Euriscus for the next 3-5 years. Good progress has been

Outputs

Output targets	
C01 – No. enterprises receiving support	120
C04 – No. enterprises receiving non-financial support	120
C08 – Employment increase in supported enterprises	25
C26 – No. enterprises cooperating with research entities	60
C28 – No. enterprises supported to introduce new products to the market	10
C29 – No. enterprises supported to introduce new to the firm products	50
Source: Output annex	

Targets to the end of Q4 2018 against achieved

Annex 1d – Health Innovation Campus

Description of the Project

The capital development of a new Health Innovation Campus at Lancaster University, including the initial building and road and infrastructure works and a revenue programme which begins related innovation collaborations with Lancashire-

Targets to the end of Q4 2018 against achieved

Outputs

Comments

Annex 1e – U Start

Description of the Project

This project seeks to deliver more resilient graduate start-up businesses contributing to the local economy particularly in priority sectors such as advanced manufacturing, low carbon energy, creative and digital, social enterprise and health sector innovation. Non-financial support includes:

- Enterprise readiness: support for potential entrepreneurs to become enterprise ready focussing on ideas testing, market research, business planning, and business formation.
- New Business: support for new business owners to de-risk their businesses and prepare them to engage in growth support including strategic planning, business leadership, securing finance and marketing – supporting the resilience of owners and business sustainability.

Project Profile	
Funding type	ERDF
Priorities sought under	3: Enhancing the competitiveness of small and medium sized enterprises

Delivery arrangements	
Leading organisation	Lancaster University
Project partners	University of Central Lancashire (UCLAN)
Geographical coverage of project	

Comments

- "There are many opportunities to attend workshops and engage in networking. I am being given support by a person with a background in the charity sector, which is really helpful."
- "I wouldn't be in business without the team at Lancaster. The 1-2-1, and peer group interactions have been really helpful. Two workshops have been useful and helped me develop new networks. The enthusiasm of the team has helped keep me motivated when I was lacking confidence to move forward. I can't fault them."
- "I now have a published book for sale and another product being developed for sale. Neither would have been achieved without the excellent advice, workshops and group work arranged by the enterprise team. The business modelling exercise at the beginning also highlighted areas I had overlooked in my original business plan and areas that I need to pay more attention to."
- "Initially really positive"… "They seemed well informed, and were encouraging but realistic. After that, I sadly didn't receive any further response, which was a real shame. I also felt unsure whether I could attend workshops or whether they were meant for people further on in the project. It wasn't so well organised on that front - maybe advice about which meetings were available would have helped."

Case Study

Case Study: Leanne (Student)

Leanne is currently studying a Ba (Hons) Business and Marketing degree at the University of Central Lancashire (UCLan) looking to become an entrepreneur upon graduation. Leanne has always had entrepreneurial drive, but realised that she did not have the knowledge to run a successful business. After hearing about the enterprise support available at UCLan, Leanne applied for a degree in order to gain the knowledge and support she needed to start her business.

Leanne came to the U Start team in 2018 with a number of business ideas. Through the business diagnostic service, Leanne was able to fully develop and refine her concepts to identify the business venture with the highest potential. Her past experience in the charity sector gave Leanne motivation to run a business which organised different projects to help support local community issues. She developed a platform to help improve opportunities for young women at a community level, including activities such as events and guest lectures and more depending on the needs of the women in the area.

Over the year working with the U Start programme, Leanne benefitted from attending a number of workshops to help her understand the practicalities of running her own business, as well as meeting contacts at networking events. Leanne also received 1-2-1 mentoring for developing her ideas further. Leanne praised the mentoring support for being very flexible, able to work around Leanne's changing needs.

"They were very flexible… I was meeting with them twice a week but now I have exams at the moment and am only able to meet once a month."

"You can give them any problem, and if they don't know the answer, they will find someone who does… go above and beyond what is expected of them."

While undertaking her degree, Leanne was able to secure funding for her business venture through the project which signposted and supported her application for an internal business fund called the Propeller Prize. Her mentor helped Leanne understand each aspect of the grant application, how she could improve one section at a time, and where she could be lean with her business operations. This ultimately led to her securing funding.

"[Her mentor] really made me think about the whole business process… make me understand where I could be more efficient with my business model."

"[The main benefit of the programme] was giving the accountability for my own work, especially when being self-employed… rather than having university deadlines, we would book in meetings where I would have to motivate myself to show what I have done and how I have made progress".

Leanne is currently studying for her finals and upon completion, will be looking to begin working on her business ideas full time, applying the knowledge she has gained from not only her degree, but also from the U Start programme.

Annex 1f – Cumbria Business Growth Hub

Description of the Project

This project aims to develop a network of SMEs, translating emerging research into practice to deliver activities relevant to businesses in their world.

The project will develop the beneficiary's capacity for the development of new innovative processes and products through a number of proven interventions including: interactive workshops and masterclasses, facilitated networking events to enhance opportunities for open innovation, student

Comments
• "The support I have received far exceeded my expectations." • "I felt it was of very high quality, hands on support. It helped us begin to analyse & understand our business strategy and the importance of having a clear strategy on determining our future direction. However, the support should be longer in order to maximise and implement the support. After a period of 6 months, goals and expectations could be assessed and then have a further 6 months of support." • "Increased confidence to innovate and grow" [as a result of support] • "The experience was very positive, particularly the peer to peer support group that has continued since the completion of the course."

Case Study

Case Study: (Anonymised Business)

Targets to the end of Q4 2018 against achieved			
Outputs	Target	Achieved	% of target achieved
R9	28	0	0%
C023	72	0	0%
Total	100	0	0%

Annex 2: Lancaster University Supported Project Headline Findings

Annex 2a – Healthcare Business Connect Lancashire

Description of the Project

This projects helps businesses working in health and life sciences with products or services of interest to the NHS make the right connections. Support is tailored to help pre start-ups, new and established businesses develop and grow their products and services through clinical and commercial assistance.

Project Profile	
Funding type	ERDF
Priorities sought under	3: Enhancing the competitiveness of

Comments

- "Receiving the reassurance that I am on the right track. I have found the support easy to access and is well tailored to my needs."
- "Excellent service could not have done it without them."
- "Would like to work closer with them to get more benefits to research."
- "The project has helped me reassess my organisation. Also, it has been very beneficial in accessing grants."

Case Study

Case Study: Mente (EMW Support Ltd)

Mente is a provider of mental health support for businesses. They offer a unique set of skills and an array of digital tools and services to help businesses manage the mental health of their employees. With approximately one in four people in the UK likely to experience some form of mental health issue each year, this is a topic of growing importance to businesses and therefore a growing business area.

Mente first contacted Lancaster University in 2017 with a novel business idea looking for a graduate a gra a greP-8

Targets to the end of Q4 2018 against achieved	
Outputs	Target

Targets to the end of Q4 2018 against achieved			
Outputs	Target	Achieved	% of target achieved
C01	16	18	113%
C05	1	2	200%
C26	11	14	127%
C29	0	0	-
C34	0	0	-
Total	28	34	121%
Based on Lancaster University figures only			

Headline Beneficiary Survey Findings

Overall 8

Comments

- "Regular contact was good. Had a lot of time talking to both academic supervisors at the start of the project where the first year of a PhD project is focussed on the set up for later years."
- "[The advisor] has been brilliant throughout, understanding our needs, communicating and ensuring were happy with the project. Ensuring a project remains useful commercially can be tricky, academics have a tendency to lose sight of the commercial application of the research. Overall, very valuable and have made plans to work with the university again."
- "The university was professional and was exactly what research should be doing connecting academics with businesses. I have made new relationships in the horticultural department and happy to work with the university again."

Case Study

Case Study: May Barn Horticultural Consultancy

May Barn Horticultural Consultancy is a Cheshire-based consultancy business for agronomy, crop production, and operational and technical management of associated horticultural processes. Founded in 2011, the business owners have over 30 years' experience in the industry which informs its work with clients in the agricultural sector, helping them develop new production techniques, plant and crop analytic interpretation, maximise crop yields and product development.

After hearing about the Eco-Innovation Cheshire and Warrington project though a business network, May Barn s]TJ 0u2.1 (B)2.3 (ar)-6.3 (n)-12.1e 9.96 -07.28 525.84 447.6 cs8.2 (n)-gj ET EM52e ne-us

Targets to the end of Q4 2018 against achieved		
Outputs	Target	Achieved

Top five benefits achieved to date
83% are more likely to engage with the University on other projects
50% have improved existing business products/processes/services
50% have raised the company profile
50% more likely to seek support through other routes
33% stronger and more stable business

Comments

- "Very happy with how the project was delivered and felt that the level of support from the supervisor from the academic supervisor was very appropriate. We could not afford the project without the support."
- "The knowledge of the researchers and the access to technology we would of not been able to use if it wasn't for the project. The centre allowed us to bridge the gap between business and academia which can be difficult."
- "It was a very straightforward process and we were able to support the business. The work has helped up move forward with a grant application from Horizon 2020 worth £50,000 to conduct more research and make some prototypes."

Annex 2e – Eco Innovation Cumbria

Description of the Project

The project targets and assists eligible SMEs to increase innovation in and adoption of low carbon technologies. Through R&D and the development of higher-level skills it aims to enable business to grow capacity in developing new products and markets enabling expansion and growth.

Project Profile	
Funding type	ERDF
Priorities sought under	4: Supporting the Shift Towards a Low Carbon Economy in All Sectors

Delivery arrangements	
Leading organisation	The University of Cumbria
Project partners	Lancaster University
Geographical coverage of project	Cumbria

Targets to the end of Q4 2018 against achieved			
Outputs	Target	Achieved	% of target achieved
C01	10	27	270%
C05	0	2	-
C26	10	16	160%
C29	7	0	0%
C34	0	0	-
Total	27	45	167%
Based on Lancaster University figures only			

Headline Beneficiary Survey Findings

Overall 14 responses were secured across the online and telephone survey.

Views on early contact	% satisfied or very satisfied
Quality of information about the available support	93%
Clarity of the eligibility criteria for receiving support	93%
Ease of the application process	86%
Length of time taken between initial inquiry to working with the project	86%

Top three reasons for engaging with support	% of respondents
New products/process development	64%
Technical skills development	36%
Gaining access to new markets	36

Comments
• "Great technical support - analysis improved R&D" • "Is a very well organised centre who are very good at finding the right person for my company and project. Have made strong contacts with the university and feel that the collaboration was natural fit." • "Initial support was good, but the project advisor's interest waned quickly. They didn't put in the right amount of time and effort into the research, and they lost focus on the objectives." • "There has been little contact with the university or the intern. When we contacted the university to say the intern hadn't been in touch since the initial meeting, the university did contact him and said that they were making progress."

Case Study

Case Study: Agronomy Research Group

Agronomy Research Group (ARG) offer consultancy services in crop production, energy efficiency and water conservation for businesses in the agricultural sector. At the time of accessing support in 2017/18, ARG was a 'pre-start up' business. The entrepreneur who set up the businesses approached Lancaster University to benefit from the "knowledge and facilities they can offer which are not available to most businesses".

The project provided ARG with a master's student looking to develop a product which can be used in water treatment to increase water conservation around the world for horticultural and amenity businesses. ARG has seen good progress on the project and enjoyed regular meetings with the university support team within the initial stages. More recent contact has been less frequent but the business leader stated that "I can always get in touch if I need anything".

ARG gave high praise for the project and the Lancaster University staff, stating that they were "very good at finding the right person for your company and project… it has been a natural fit to use the centre [Centre for Global Eco-Innovation] as a middle man between businesses and the university".

As a result of working on the project, ARG has seen their business become stronger and more stable, raising the company profile through the development of a new product. With a successful water treatment project in sight, AGR are anticipating future revenues of between £3-5 million over the next few years in addition to offering the current master's student an employment opportunity to carry on their work.

Annex 3 – Summative Assessment Standard Spend and

Cumbria Innovations Platform

Standard Table Format: Spend and Output Performance		
Indicator	Targets	Performance at Time of Evaluation

Lancashire Forum

Standard Table Format: Spend and Output Performance				
Indicator	Targets	Performance at Time of Evaluation	Projected Performance at Project Closure	Overall Assessment
				Assess

Health Innovation Campus

Standard Table Format: Spend and Output Performance							
Indicator	Targets		Performance at Time of Evaluation		Projected Performance at Project Closure		Overall Assessment
	Original	Adjusted	Number	% of Target	Number	% of Target	
Capital Expenditure (£m)	£12,099,124	£12,099,124	£3,209,223	27%	£12,099,124	100%	
Revenue Expenditure (£m)	£2,000,000	£2,000,000	£350,392	18%	£2,000,000	100%	
(C1) Number of enterprises receiving support	300	300	36	12%	300	100%	

Cumbria Business Growth Hub

Standard Table Format: Spend and Output Performance							
Indicator	Targets		Performance at Time of Evaluation		Projected Performance at Project Closure		Overall Assessment
	Original	Adjusted	Number	% of Target	Number	% of Target	
Capital Expenditure (£m)	£0	£0	£0	-	£0	-	
Revenue Expenditure (£m)	£1,124,288	£955,643	£653,875	68%	£653,875	68%	
(C1) Number of enterprises receiving support	70	70	74	106%	74	106%	
(C4) Number of enterprises receiving non–financial support	70	70	74	106%	74	106%	
(C5) Number of new enterprises supported	0		1	-	1	-	
(C8) Employment							

Annex 4 – Project Level Impacts

The standard table format gross and net impact tables are provided below for the six Lancaster University led ERDF projects. The details are also contained in the Excel summative assessment summaries that accompany this report.

Local -i

Standard Table For mat: Gross and Net Additional Impact for Employment and GVA	
	Impact Area 1:
	Lancashire LEP

Cumbria Innovations Platform

Lancashire Forum

Standard Table Format: Gross and Net Additional Impact for Employment and GVA			
		Impact Area 1: Lancashire LEP	
		Measure	Adjustment
Impact Indicator: Employment Unit = FTEs	Gross Impact	1,087	Estimate derived from survey data for created and safeguarded jobs to date and in the future (to the end of 2023)
	Deadweight / reference case	574	47% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Displacement / substitution	449	21% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Leakage	376	16% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Net Additional	470	Multiplier: 1.25 - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
Impact Indicator: GVA Unit = £m	Gross Impact	£201,682,180	Lancashire economy-wide average GVA per FTE 2017 applied to employment impacts, persisting for three years
	Deadweight / reference case	£106,488,191	47% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Displacement / substitution	£83,408,473	21% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Leakage	£69,812,892	16% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015Ï-q HY ÀT„ p

Health Innovation Campus

Standard Table Format: Gross and Net Additional Impact for Employment and GVA		
		Impact Area 1: Lancashire LEP Measure

Cumbria Business Growth Hub

Standard Table Format: Gross and Net Additional Impact for Employment and GVA			
		Impact Area 1: Cumbria LEP	
		Measure	Adjustment
Impact Indicator: Employment Unit = FTEs	Gross Impact	519	Estimate derived from survey data for created and safeguarded jobs to date and in the future (to the end of 2023)
	Deadweight / reference case	274	47% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Displacement / substitution	215	21% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015
	Leakage	180	16% - Mean sub-regional benchmark for business development & competitiveness, HCA Additionality Guidance 2015

N.7 (op2 re fj 0 Tc .24 0.48 40.32 re f 277.92 53ddi)-03.3 0 N
